

Leonia Municipal Bldg. | Flash Report No. 27 – Dec 05, 2022



PROJECT HIGHLIGHTS

Project Overview


- Design – Construction Documents completed 1/17
- General Contractor agreement executed 4/19
- Ground Breaking – 5/15
- GC Mobilization – 5/23
- Civil engineer – Site work ongoing
- Change order requests - Ongoing
- Schedule – Project on Schedule
- IT/AV/Security – Design planning - Ongoing
- Furniture – Ongoing
- Third party inspector – Metro Awarded Contract
- Parking lot logistics – Ongoing
- Unsuitable Soil Removal - Completed

KEY ACTIVITY FORECAST

Two Week Look Ahead:

- Under ground sanitary and Storm piping
- Under ground Electrical
- Inspection, back fill and grade to sub slab
- East masonry exterior wall,
- Change order approvals
- Facilities Committee Meeting – 12/22

PROJECT TIMELINE

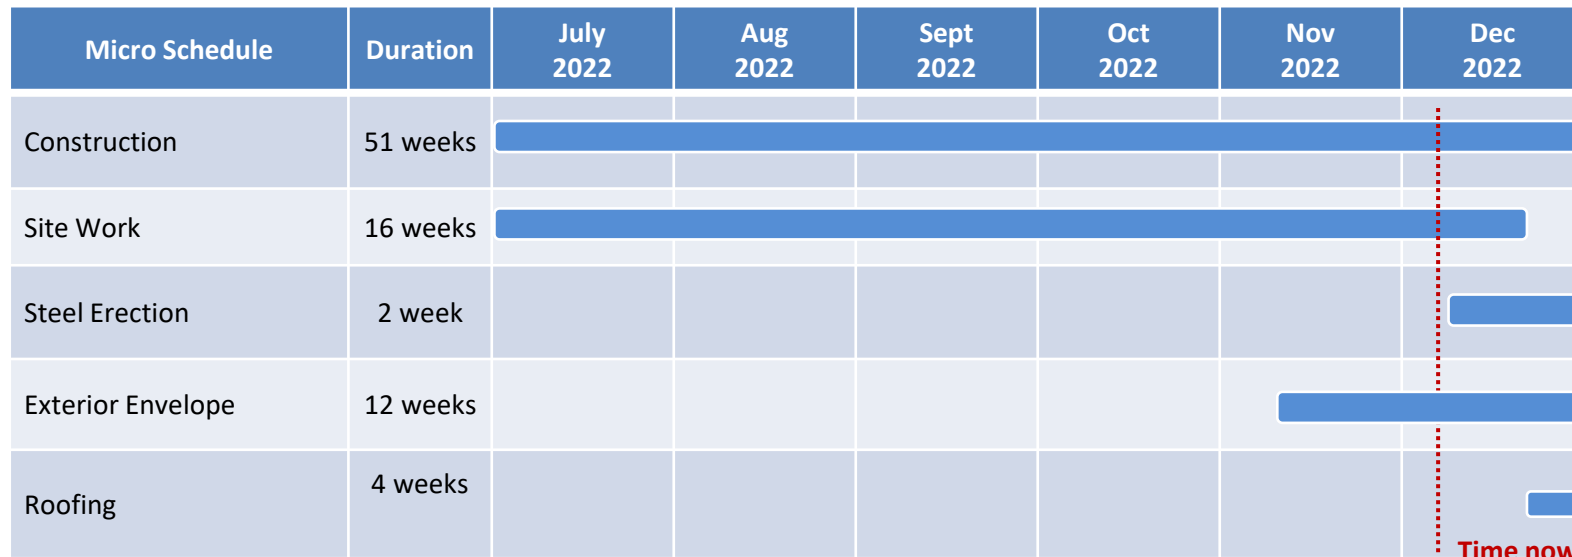

KEY ISSUES

Key Issues

- Timeline – Adhere to master schedule and milestones
- Delays – RFI Clarification and timely decisions
- Change orders – Review and execute
- Shop Drawings – submittal process
- Construction –
 - Long Lead Items
 - Testing & decisions
 - Geo tech compliance

CRITICAL PATH

Critical Path Schedule (Tasks)

- Special inspections
- Geo tech review and recommendations
- Construction Continuation
- Submittals & RFI approvals
- Supply chain & substitution procurement strategy
- Construction Harmony
- Furniture advisory
- IT/AV/Security advisory

KEY RISKS

Risks

- Material escalations & Shortages
- IT / AV / Sec Contractor Onboarding

Risk Mitigation

- Identify long lead items
- Cost control milestones
- Change order mitigation
- Furniture design/ procurement & Selections
- Security / IT/ AV Design requirements
- Design team time management
- Construction team management
- Change order resolution & Execution

COST SUMMARY

Item	Budget	Actual	
CONSTRUCTION	\$10,355,133	\$7,605,172	↓
CONSULTANTS 10%	\$1,293,251	\$1,034,295	↓
FURN / APPLIANCE SIGNAGE	\$335,645	\$341,668	↑
IT/AV/SECURITY	\$254,925	\$396,761	↑
MISCELLANEOUS FEES	\$38,239	\$38,239	↓
DEMOLITION & REMEDIATION	\$801,479	\$221,471	↓
PROPERTY ACQUISITION	\$1,476,000	\$1,476,000	↓
TOTAL	\$ 14,554,672	\$11,113,606	↓

INTERIOR RENO.

Interior Renovation (Existing Bldg.)	Budget
INTERIOR CONSTRUCTION	\$1,500,000
CONSULTANTS 10%	\$150,000
CONTINGENCY / ESCALATION 10%	\$165,000
TOTAL	\$1,815,000

Overall Project Status

Orange

