

Leonia Municipal Bldg. | Flash Report No. 36 – May 19, 2023



PROJECT HIGHLIGHTS

Project Overview


- Design – Construction Documents completed 1/17
- Change order requests - Ongoing
- Schedule – Contractor to schedule update
- Slab Concrete Pour Completed
- Signage – Decision In Progress
- GZA Remediation – Additional Monitoring Wells Installed
- IT/AV/Security – Contractor Onboarded
- Furniture – Changes provided
- Leveraged CBRE Fusion Partnership for early delivery of generator

KEY ACTIVITY FORECAST

Two Week Look Ahead:

- Finish Roof Blocking (5/19)
- Finish West Framing
- Start North and South Walls Sheathing
- Start Interior Framing
- Start second floor sprinkler piping
- Start Installing Roof Insulation
- Install RTU and unit curbs
- Coordinate Telecom & Pole removal
- Change order approvals
- Facilities Committee Meeting – 05/25

PROJECT TIMELINE

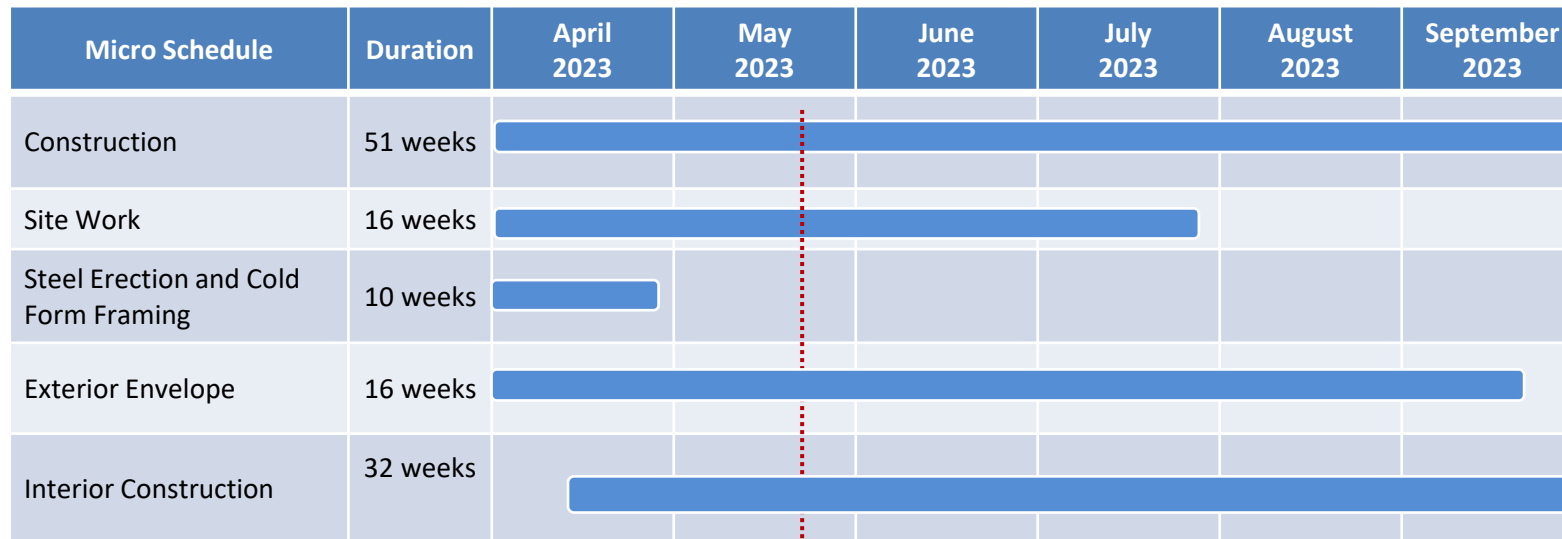

KEY ISSUES

Key Issues

- Timeline – Adhere to master schedule and milestones
- Delays – RFI Clarification and timely decisions
- Change orders – Review and execute
- Shop Drawings – submittal process
- Construction –
 - Long Lead Items
 - Testing & decisions
 - Geo tech compliance

CRITICAL PATH

Critical Path Schedule (Tasks)

- Special inspections
- Geo tech review and recommendations
- Construction Building Envelope
- Submittals & RFI approvals
- Change Order Approvals
- Supply chain & substitution procurement strategy
- Construction Harmony

KEY RISKS

Risks

- Material escalations & Shortages
- Exterior Metal Panel and Brick Delivery

Risk Mitigation

- Identify long lead items
- Cost control milestones
- Change order mitigation
- Floor selections and Carpet substitutions/LVT
- Security / IT/ AV Design approval
- Design team time management
- Construction team management
- Change order resolution & Execution

COST SUMMARY

Item	Budget	Actual	
CONSTRUCTION	\$10,355,133	\$8,489,941	↓
CONSULTANTS 10%	\$1,293,251	\$1,034,295	↓
FURN / APPLIANCE SIGNAGE	\$335,645	\$335,645	↓
IT/AV/SECURITY	\$254,925	\$431,577	↑
MISCELLANEOUS FEES	\$38,239	\$89,741	↓
DEMOLITION & REMEDIATION	\$801,479	\$271,471	↓
PROPERTY ACQUISITION	\$1,476,000	\$1,476,000	↓
TOTAL	\$ 14,554,672	\$12,128,670	↓

INTERIOR RENO.

Interior Renovation (Existing Bldg.)	Budget
INTERIOR CONSTRUCTION	\$1,500,000
CONSULTANTS 10%	\$150,000
CONTINGENCY / ESCALATION 10%	\$165,000
TOTAL	\$1,815,000

Overall Project Status

Orange

